

CRITICAL PATH ANALYSIS

Project Infrastructure Alpha - Phase 2

Revision 1.0.4


Project Manager **Alexander Wright**


Start Date **2023-10-01**

Est. Completion **2024-03-15**

ID	ACTIVITY DESCRIPTION	DURATION (DAYS)	PREDECESSORS	FLOAT (SLACK)	STATUS
A1	Site Survey & Geotech Analysis	14	-	0	CRITICAL
A2	Environmental Permit Filing	30	-	12	On Track
B1	Structural Engineering Design	25	A1	0	CRITICAL
B2	Material Procurement (Long Lead)	45	B1	0	CRITICAL
C1	Utility Grid Mapping	10	A1	5	Pending
D1	Foundational Concrete Pour	20	B2, C1	0	CRITICAL

NETWORK LOGIC DIAGRAM



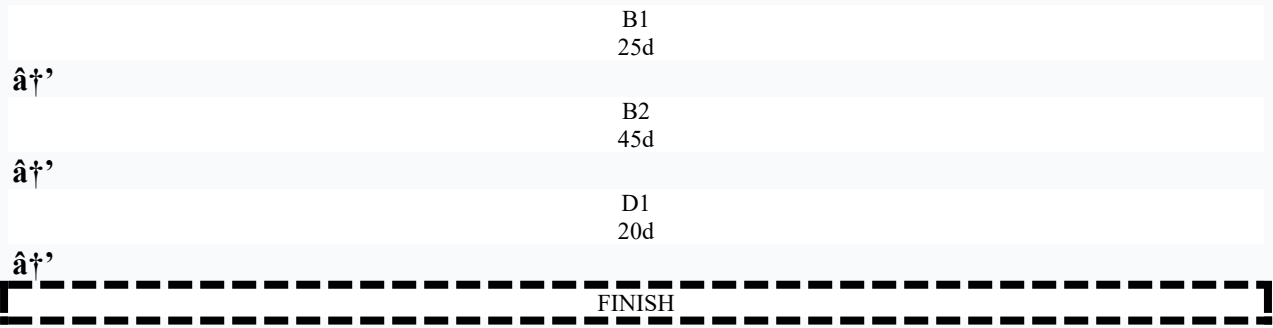

** Red outlines denote the critical path. Any delay in these tasks will delay the project completion.*

Print Report
